

C.E. Williams Middle School

PROJECT TEAM

Construction Management:

Cumming

Project Manager:

Bobby Bryant

Site Manager:


Chuck Lather

Architect:

LS3P

General Contractor:

Contract Construction

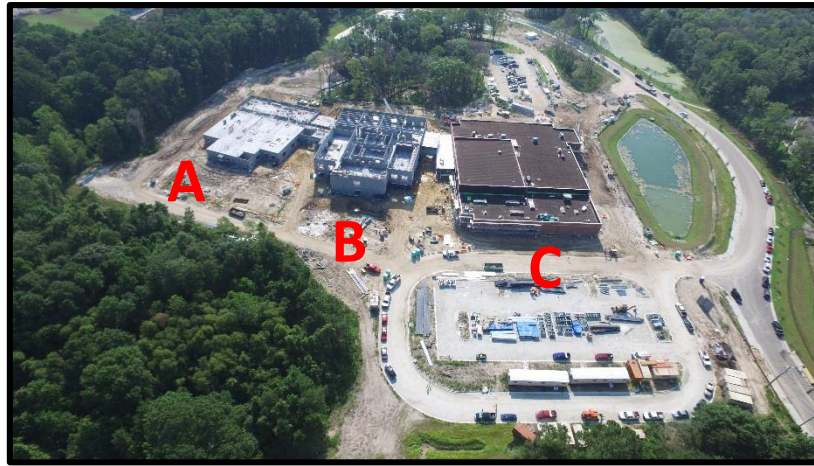

PROJECT UPDATE 7/10/2019

Contract Construction has accomplished the following building construction:

- Building "C" Hood, Freezer, and UDS 70% Complete
- Building "C" Exterior Brick 70% Complete
- Building "C" Build CMU Interior Walls 95% Complete
- Building "B" CMU Walls (thru 2nd floor) 60% Complete
- Building "B" Elect. & Mech. Rough-In 65% Complete
- Building "A" CMU Walls (thru 2nd floor) 55% Complete
- Building "A" Elect. & Mech. Rough-In 50% Complete

This project will be completed for 2020-2021 school year.

PROJECT DATA

Scope: Provide a new 137,227 SF two-story facility to serve 900 students, next to the West Ashley High School.

Project Budget: \$53.3 Million

Schedule:

Design completion: May 2018

Construction start: Aug 2018

Construction completion: Aug 2020

Square Footage: 137,227 SF

Site Size: 32 acres

